




Cross Inlet - Pipeline Installation

Proposed Configuration

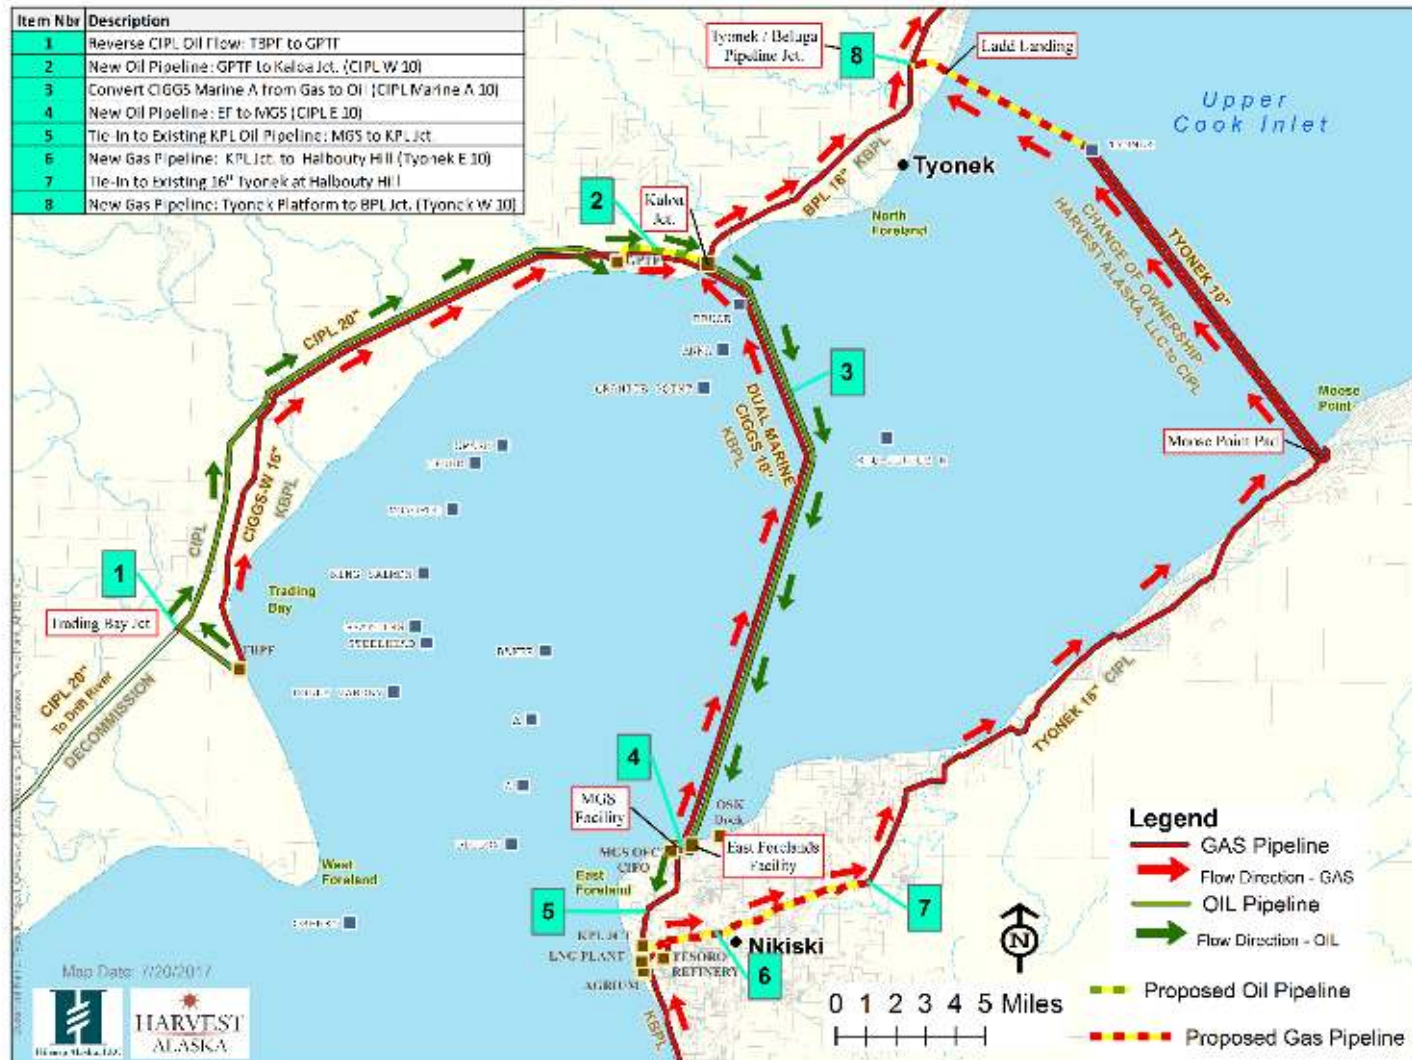

Harvest Alaska Cross Inlet - Pipeline Installation

Gas Status:

- Tyonek Platform to Beluga Pipeline:
 - Pipe Pull Complete
 - Subsea Tie-ins, Est. Comp. Sept. 15
- Ladd to BPL: Complete
- KPL Junction to Hallibouty Hill: Complete
- Estimated First Gas: Sept. 20

Harvest Alaska Cross Inlet - Pipeline Installation



Gas

Harvest Alaska Cross Inlet - Pipeline Installation

Oil Status:

- Granite Pt to Kaloa: Mechanically Complete, Fiber Optics Remaining
- East Forelands to MGS: Complete
- MGS to KPL – LP CIGG's (Hydro Testing)
- Estimated First Oil: Late September Early October

Harvest Alaska Cross Inlet - Pipeline Installation



Oil

