


# Tyonek -> BPL: Ladd Landing



# Proposed Configuration

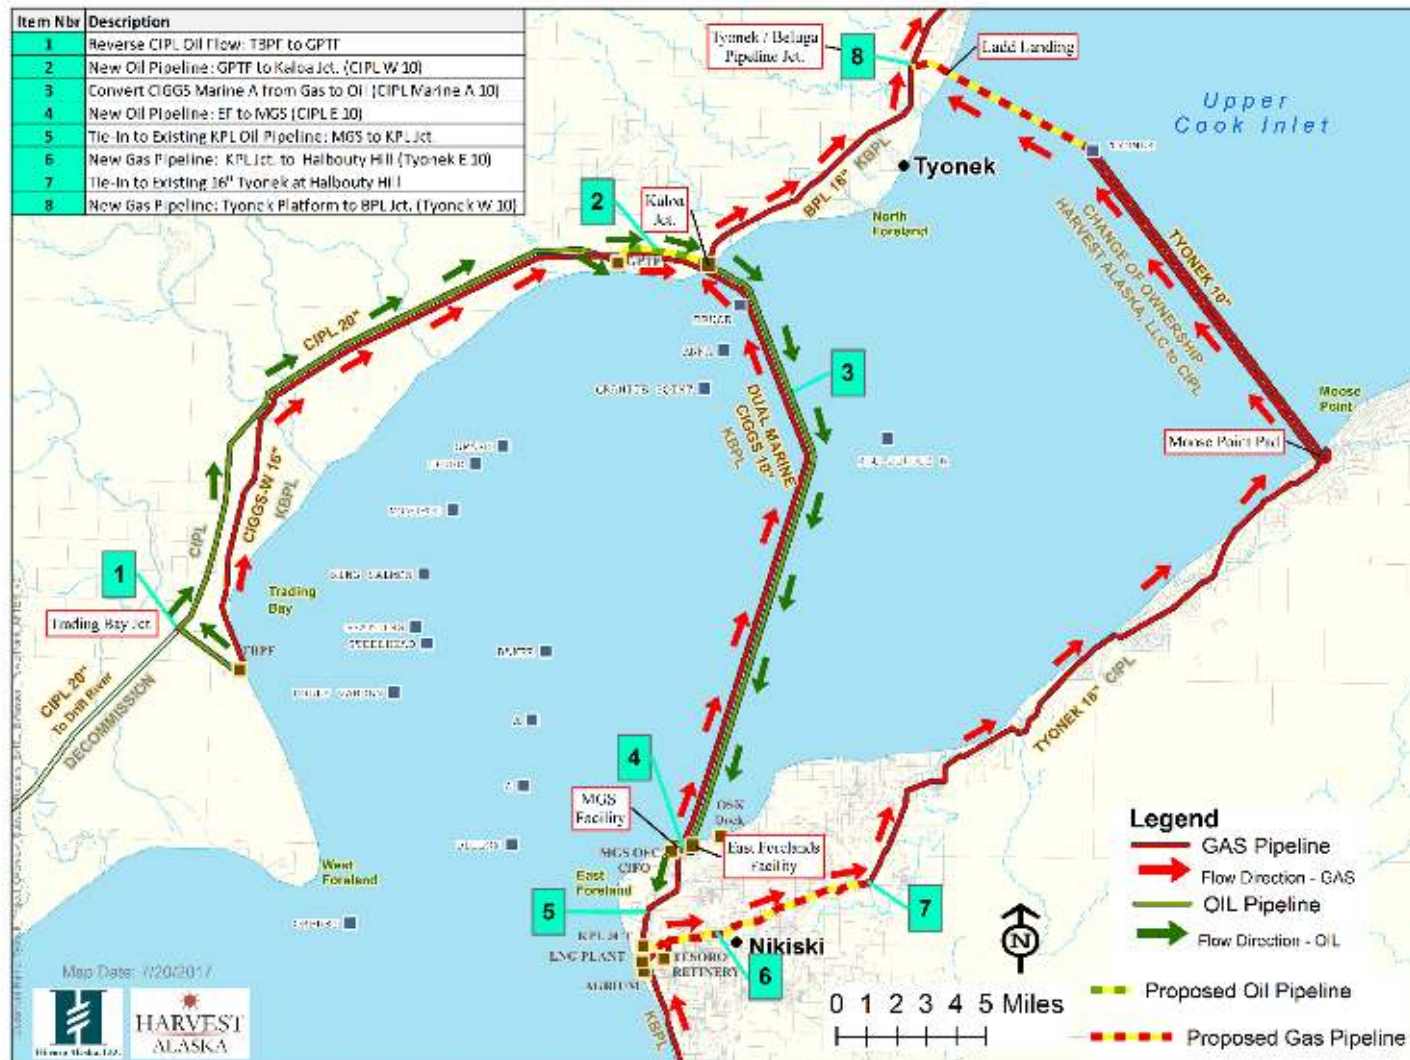

# Harvest Alaska – CIPL Cross Inlet Extension

## Status:

- Granite Pt to Kaloa: 80% Comp., Est. Comp. May 1<sup>st</sup>
- Tyonek Platform to Beluga Pipeline:
  - Prefabrication 20% Complete
  - Marine Assets Arrive May 15th
  - Off-Shore Pull Begins June 1<sup>st</sup>
  - Est. Comp. August 1<sup>st</sup>
- East Forelands to MGS: 80% Comp, Est. Comp. May 1<sup>st</sup>
- KPL Junct. to Halibouty Hill: 20% Comp., Est. Comp. June 1st
- Estimated First Oil: Late September
